

Project Plan

ShiftLite

Industry Partner	N/A
Primary Instructor	Anjana Shah
Team Member	Maddox Duggan
Team Member	Myles Romans Muirhead
Team Member	Aaron Sabilano

Document Revision History

Revision #	Date	Description
0.1	2025-05-07	Initial Project Plan (Sprint 2 submission)
2.0	2026-02-08	Revised Project Plan – Sprint 5 status update, scope and timeline adjustments

Table of Contents

Table of Contents.....	1
Revision Summary (Sprint 5).....	2
1. Executive Summary.....	4

2. Project Approvers, Reviews and Distribution List	5
3. Scope.....	5
4. Deliverables	6
5. Assumptions	6
6. Dependencies.....	7
7. Risk Management	8
8. Communication	9
9. Task Listing (WBS- Work Breakdown Structure)	10
10. Gantt Chart.....	11
11. Milestones.....	12
12. Responsibility Assignment Matrix (R.A.M.)	13
13. Approval.....	14

Revision Summary (Sprint 5)

This revision updates the original Sprint 2 Project Plan to reflect the current understanding and direction of the project as of Sprint 5.

Key revisions include:

- A refined project objective
 - Emphasis on overall management efficiency rather than communication.

- Updated scope definitions
 - To support short, task-focused user interactions and rapid information access.
- Adjusted deliverables to align with the current MVP priorities.
- Revised task statuses, milestones, and timelines based on completed and in-progress sprint work.
- Alignment of the project completion date with the planned end date of April 2, 2026.

1. Executive Summary

The following describes the project to be executed.

Objective	The objective of this project is to design and develop a mobile management application that increases overall operational efficiency in fast-paced hospitality environments. Rather than acting as a communication-heavy platform, the application is intended to support quick, focused interactions that allow users to complete tasks in under one minute per session. The system prioritizes clarity, speed, and usability by enabling staff and managers to quickly view information, take action, and return to their responsibilities with minimal disruption. Core goals include streamlined task handling, efficient inventory oversight, role-based dashboards, and high-visibility alerts and notifications that demand attention when necessary. Filtering, sorting, and search functionality are emphasized throughout the application to ensure information is immediately accessible and actionable. <i>(Updated in Sprint 5 to reflect refined project focus on management efficiency and rapid task-based interactions.)</i>
Corporate Goals Addressed	Operational Efficiency Improvement – Reduce time spent navigating the application by ensuring all core actions are quick, readable, and accessible, minimizing disruption during peak service hours. Management Effectiveness – Provide managers with clear visibility into tasks, inventory, and staff activity through concise dashboards and actionable alerts. Information Accessibility – Enable fast decision-making by implementing filtering, sorting, and search capabilities across all major data views. Attention Management – Ensure alerts and notifications are visually distinct and attention-grabbing, preventing critical updates from blending into routine interface elements. <i>(Updated in Sprint 5 based on usability insights and evolving project direction.)</i>
Planned Start Date	Wednesday, September 10, 2025

Planned End Date	Thursday, April 2, 2026
------------------	-------------------------

2. Project Approvers, Reviews and Distribution List

Approvers, reviewers and distribution list

Project Role	Name	E-mail	Date
Team member	Myles Romans	101485291@georgebrown.ca	2025-05-07
Team member	Maddox Duggan	101483006@georgebrown.ca	2025-05-07
Team member	Aaron Sabilano	101016762@georgebrown.ca	2025-05-07

3. Scope

In Scope	Out of Scope
<i>(The scope has been refined in Sprint 5 to prioritize speed, clarity, and minimal user interaction time.)</i>	
Development of Mobile interfaces for staff communication	Payment Processing/Customer facing features
Integration of Inventory tracking	All forms of hardware(e.g., tablets, buzzers).
Development of Task/Table Management features	Integration with financial/payroll systems
Role-Based Access for staff members	External booking and reservation systems
Implementation of Secure user log-in	Third-party integrations outside of the defined operations framework
User interactions designed for short, task-focused sessions (typically under one minute)	
High-visibility notifications and alerts designed to immediately capture user attention	
Filtering, sorting, and search functionality across tasks, inventory, and staff views	

Role-based dashboards optimized for quick information scanning and decision-making	
<i>(Updated in Sprint 5 based on usability insights and evolving project direction.)</i>	

4. Deliverables

(Deliverables revised in Sprint 5 to reflect current MVP priorities and feasibility.)

This project will deliver the following:

Deliverable	Description
Mobile Application	A mobile application designed for short, task-focused interactions, allowing staff and managers to quickly view information, act, and return to their responsibilities with minimal disruption.
Inventory Tracking System	A streamlined inventory tracking interface that allows users to quickly view stock levels, apply filters or searches, and perform updates efficiently without navigating complex workflows.
Staff Communication system - Alert System	A lightweight alert and notification system designed to deliver high-visibility updates and reminders without requiring extended in-app communication or prolonged user engagement.
Management Features	Role-based management tools that provide concise dashboards, quick status visibility, and actionable controls to improve oversight and decision-making efficiency.
<i>(Deliverable descriptions updated in Sprint 5 to emphasize efficiency-focused design and MVP scope.)</i>	

5. Assumptions

This project makes the following assumptions;

- Team members will be to complete project deliverables according to the assigned deadlines
- Management of the businesses adopting the application will support the adoption of the new system.
- Internet connection within the service areas will be sufficient to support the features of the application
- Required tools used in development of the application remain stable throughout the project.

- All user data and information will be handled in accordance to applicable privacy and security policies
- The Project Plan may change as new information becomes available

6. Dependencies

The following are the internal and external dependencies that will have to be acknowledged and addressed;

- Mobile devices used by staff are available and reliable.
- Compliance with all relevant regulations e.g. data privacy, workplace safety.
- Operational areas have reliable Wi-Fi/network coverage.
- Managers will be active in the process of adopting the new application
- Access to a secure server for hosting and storage of data

7. Risk Management

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
Technical Challenges	High	High	Test modules early, leverage version control and perform code reviews regularly
Team Communication Issues	Medium	Low	Establish weekly structured progress meetings and use shared online workspaces to maintain transparency.
Development delays	High	Medium	Ensure deadlines are realistic, monitor progress of individual assignments weekly and integrate buffer time into the project timeline.
Limited development time	Medium	High	Prioritize completion of core features advanced features are to be left for future iterations.

8. Communication

Reporting

The following reports will be produced;

Report	Audience	Frequency
Progress Report	All Team Members	Weekly
Testing/Evaluation Report	All Team Members	At the end of each development phase

Meetings


The following meetings/communication will be established;

Meeting	Purpose	Attendees	Frequency
Spring Planning Meeting	Delegate tasks for the upcoming sprint, clarify priorities and set deadlines	All Team Members	At the beginning of each sprint
Progress Meeting	Review progress of assigned tasks, discuss challenges faced and ensure team is aligned with the timeline.	All Team Members	Weekly

9. Task Listing (WBS- Work Breakdown Structure)

(Task statuses updated in Sprint 5 to reflect completed, in-progress, and deferred work.)

The following resource planning proposal template summarizes the resource hours committed to this project, upon final approval of this document.

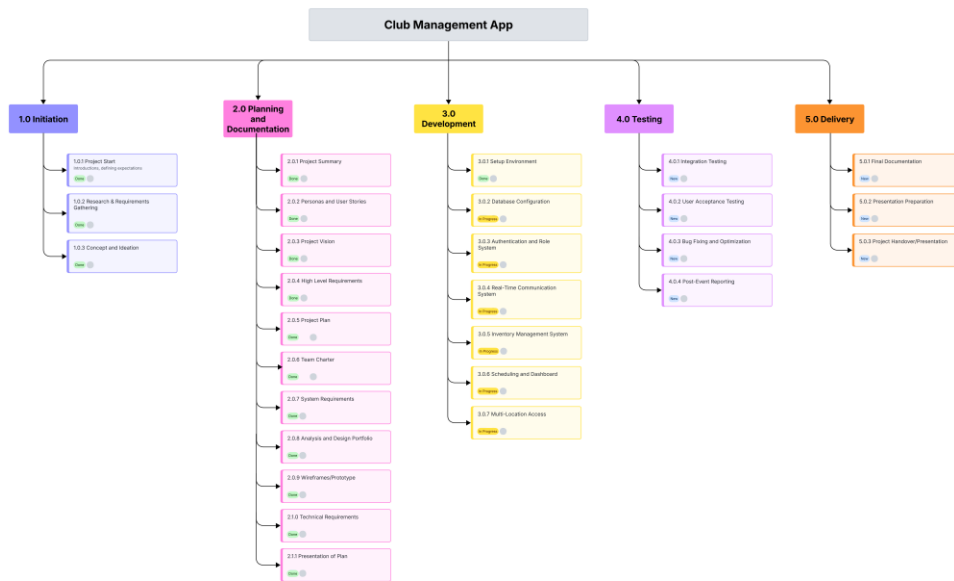


WBS ID	Task Name	Sprint	Dependencies	Status
1.0	Initiation Phase	Pre-Sprint	–	Complete
1.01	Project Start	Pre-Sprint	–	Complete
1.02	Research & Requirements Gathering	Pre-Sprint	1.01	Complete
1.03	Concept and Ideation	Pre-Sprint	1.02	Complete
2.0	Planning & Documentation Phase	Sprint 1	1.0	In Progress
2.01	Project Summary	Sprint 1	1.0	Complete
2.02	Personas and User Stories	Sprint 1	2.01	Complete
2.03	Project Vision	Sprint 1	2.02	Complete
2.04	High-Level Requirements	Sprint 1	2.03	Complete
2.05	Project Plan	Sprint 2	2.04	Complete (Revised in Sprint 5)

2.06	Team Charter	Sprint 2	2.05	Complete
2.07	System Requirements	Sprint 3	2.05	Complete
2.08	Analysis & Design Portfolio	Sprint 3	2.06	Complete
2.09	Wireframes / Prototype	Sprint 4	2.08	Complete
2.1.0	Technical Requirements	Sprint 4	2.09	Complete
2.1.1	Presentation of Plan	-		Complete
3.0	Development Phase	-	2.0	In Progress
3.01	Setup Environment	-	2.0	Complete
3.02	Database Configuration	-	3.01	Complete
3.03	Authentication and Role System	-	3.02	In Progress
3.04	Real-Time Communication System	-	3.03	In Progress
3.05	Inventory Management System	-	3.04	In Progress
3.06	Scheduling and Dashboard	-	3.05	In Progress
3.07	Multi-Location Access	-	3.06	In Progress
4.0	Testing Phase	-	3.0	Not Started
4.01	Integration Testing	-	3.0	Not Started
4.02	User Acceptance Testing	-	4.01	Not Started
4.03	Bug Fixing and Optimization	-	4.02	Not Started
4.04	Post-Event Reporting	-	4.03	Not Started
5.0	Delivery Phase	-	4.0	Not Started
5.01	Final Documentation	-	4.0	Not Started
5.02	Presentation Preparation	-	5.01	Not Started
5.03	Project Handover / Presentation	-	5.02	Not Started

10. Gantt Chart

(The Gantt chart was updated in Sprint 5 to align with the revised project timeline and planned completion date of April 2, 2026.)

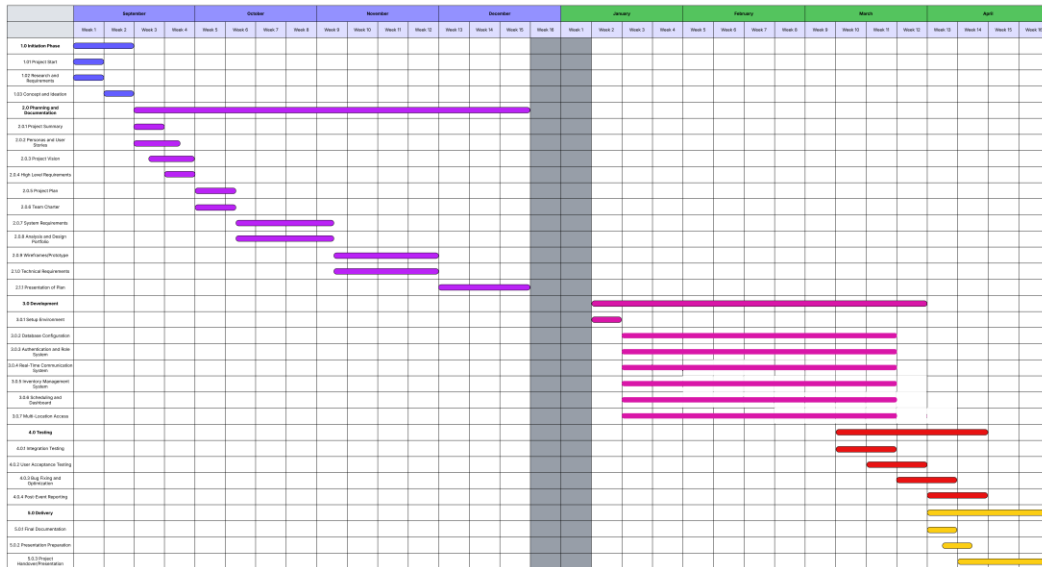

11. Milestones

(Milestones revised in Sprint 5 to align with updated project timeline and completion date.)

Major Activity or Milestone	Estimated Milestone Target date	Team Members
Completion of Planning/ Documentation Phase	Sprint 5 (February 2026)	• Myles • Aaron • Maddox
Completion of Development Phase	March 2026	• Myles • Aaron • Maddox
Project Handover/Presentation	April 2, 2026	• Myles • Aaron • Maddox
<i>(Milestones updated in Sprint 5 to align with the revised project timeline.)</i>		

12. Responsibility Assignment Matrix (R.A.M.)

WBS ID / Task Name	Primary	Secondary
1.0 – Initiation Phase	Maddox	Aaron
1.01 – Project Start	Maddox	Aaron
1.02 – Research & Requirements Gathering	Aaron	Myles
1.03 – Concept and Ideation	Aaron	Maddox
2.0 – Planning & Documentation Phase	Maddox	Aaron
2.01 – Project Summary	Myles	Maddox
2.02 – Personas and User Stories	Aaron	Maddox
2.03 – Project Vision	Maddox	Myles
2.04 – High-Level Requirements	Aaron	Myles
2.05 – Project Plan	Myles	Maddox
2.06 – Team Charter	Aaron	Aaron
2.07 – System Requirements	Aaron	Myles
2.08 – Analysis & Design Portfolio	Maddox	Aaron
2.09 – Wireframes / Prototype	Maddox	Myles
2.10 – Technical Requirements	Aaron	Myles
2.11 – Presentation of Plan	Myles	Maddox
3.0 – Development Phase	Myles	Aaron
3.01 – Setup Environment	Myles	Aaron
3.02 – Database Configuration	Aaron	Myles
3.03 – Authentication and Role System	Aaron	Maddox
3.04 – Real-Time Communication System	Myles	Aaron
3.05 – Inventory Management System	Aaron	Myles
3.06 – Scheduling and Dashboard	Maddox	Myles
3.07 – Multi-Location Access	Myles	Aaron
4.0 – Testing Phase	Aaron	Maddox
4.01 – Integration Testing	Aaron	Myles
4.02 – User Acceptance Testing	Myles	Maddox
4.03 – Bug Fixing and Optimization	Maddox	Aaron
4.04 – Post-Event Reporting	Aaron	Myles
5.0 – Delivery Phase	Maddox	Myles
5.01 – Final Documentation	Maddox	Aaron
5.02 – Presentation Preparation	Myles	Maddox
5.03 – Project Handover / Presentation	Maddox	Myles

13. Approval

(This document reflects the most current approved version of the project plan as of Sprint 5.)

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date
Team member	Myles Romans Muirhead	Myles Romans Muirhead	2026-02-08
Team member	Maddox Duggan	Maddox Duggan	2026-02-08
Team member	Aaron Sabilano	Aaron Sabilano	2026-02-08
